

## SPD PROJECT



## SPD PROJECT





## SPD PROJECT



### *Implementation of the Ottawa Convention through the disposal of Anti-Personal Mines in Stock Article-4*

**FINANCIAL SUPPORT OF EC**



## SPD PROJECT



### **OBJECTIVES**

To fulfill with Article 4 of the Ottawa Convention, ratified by the Angolan Government and made into force in December 2002, aiming at the disposal of all Anti-Personal landmines in stock within 4 years by January 2007; and

To develop the capacity building of the national authority, CNIDAH, and the operators, state bodies, FAA and INAD to carry out the operation of destruction of the AP mines in stock in accordance with mine action international humanitarian standards.



## SPD PROJECT



### Profile of the Project

- Timeframe: *maximum 2 years (01/01/05 - 31/12/06)*
- Areas of intervention: the whole country
- Total Budget: *EUR 1,765,000*
- Execution modality: *NEX (National Execution)*
- Partners of the project: *4*
- Plan of Action: *5 phases*



## SPD PROJECT



### Budget for the Project

The Project is co-financed by 3 parties as follows:

EC: *EUR 1,500,000 (85%)*



GoA: *EUR 170,000 (10%)*

UNDP: *EUR 95,000 (5%)*

---

*Total EUR 1,765,000*

*At least 10 % of the project budget needs to be funded by other partners than EC ( EC regulations)*

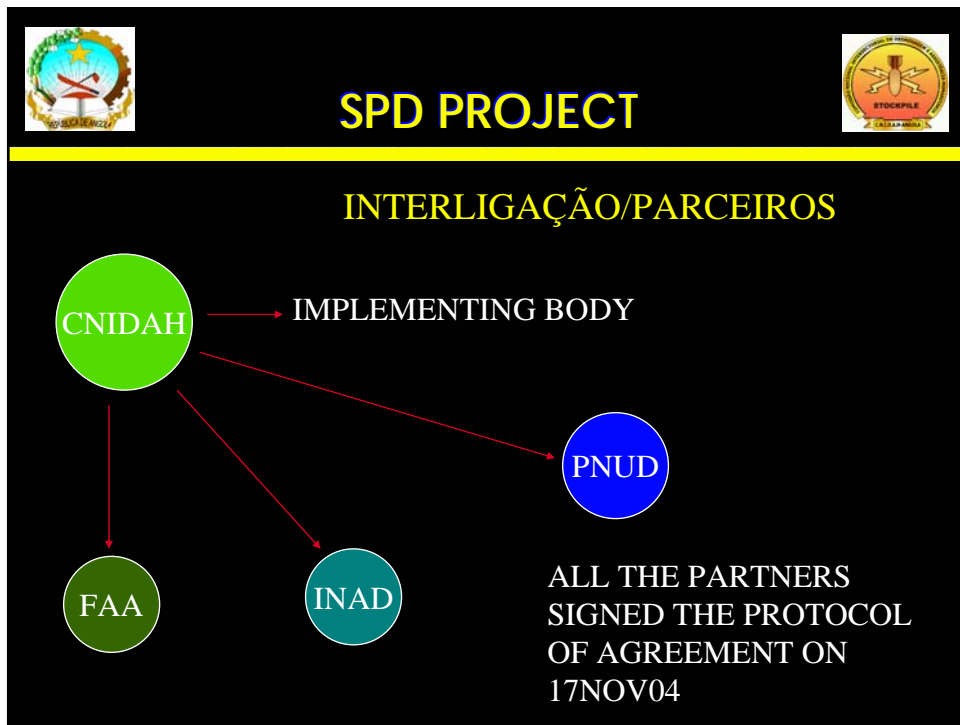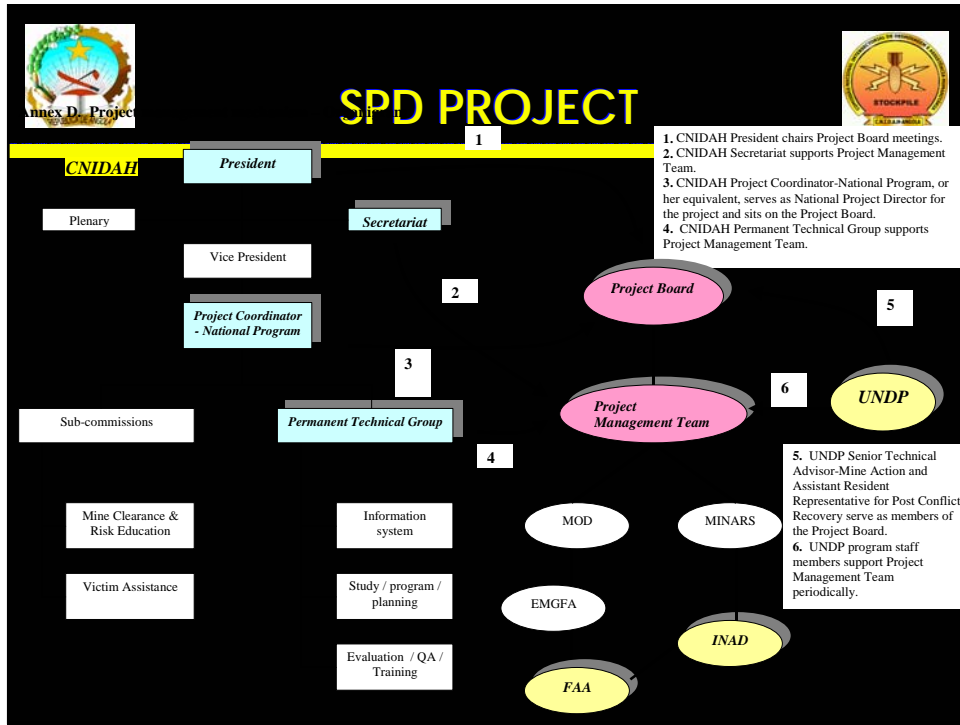



## SPD PROJECT



### INTRODUCTION OF THE PROJECT TEAM

Dr. Adriano Gonçalves – National Director of the Project

Brig/Eng. Roque de Oliveira – Project Manager

João Udengue – Financial and administrative Assistant

Manuel Bitacama – Technical Assistant

Espírito Santo – Technical Assistant

Joaquim Merca – Technical Advisor

Keita Sugimoto – UNDP Projects Officer



## SPD PROJECT



### EVOLUTION/INTERLINK

End of March 2005 UNDP Headquarters informed the reception of equivalent to 950.000 Euros from EC, funds for this project.  
It was confirmed in Apr05, 1, 254,953,76 USD

1st week of May05, UNDP Angola accomplished the ATLAS System and the first phase of the project started



## SPD PROJECT



### Trend Principles

#### "Sustainability"

##### Institutional Sustainability :

The organizational structure created for this project will be maintained by the partners as long as it continues to be relevant to the government necessities in addressing the matter of AP mines in stock.

##### Financial Sustainability :

Should the project has necessity to continue beyond the second year period, the government has to allocate financial resources for current expenses to cover a short period, and capital investment costs and current expenses if the extension period for the project becomes longer.

=> if needed, the government will be encouraged to increase its level of financial contribution to the project.



## PROJECTO SPD



### Trend Principles

#### "Empowerment"

At the completion of the project, CNIDAH, FAA and INAD will have the capacity to transfer the know-how to other affected countries and support them in the implementation of the Article 4 of the Ottawa Convention.

#### "Participation"

The project aims to complete the disposal of stocked AP mines. Therefore, the project includes all relevant partners and must be able to obtain the data from every AP in stock that exist at the moment under jurisdiction or control of the Angolan Government.



# SPD PROJECT



## PLAN OF ACTION

Year 1

Activity	1 Month	2	3	4	5	6	7	8	9	10	11	12	IMPLEMENTOR
1st Preparation	█												CNIDAH, PNUD
2nd Planification, Coordination and Training	█	█											CNIDAH, PNUD, FAA, INAD
3rd Survey and Analyse Of the AP mines in Stock		█	█	█	█								FAA, CNIDAH, PNUD
4th Review, tests and training				█	█	█							CNIDAH, PNUD, FAA, INAD
5th Execution (destruction of AP mines in Stock)							█	█	█	█	█	█	FAA, CNIDAH, PNUD
Assessment & monitoring	█	█	█	█	█	█	█	█	█	█	█	█	CNIDAH, PNUD



# SPD PROJECT



## ACTIVITIES IN 2005

Training courses:

- Demilitarization of Explosive Ordnance;
- Technical Survey and Assessment;
- Reconversion of Military Demining Into Humanitarian



## PROJECTO SPD



### ACTIVITIES IN 2005

Analysis of information available about the location of stockpiled artefacts containing AP as well as its types;

Analysis of the techniques to be applied in the third phase of the project



## PROJECTO SPD



### ACTIVITIES IN 2005

Preparation of a demolition Course to be implemented in the fourth phase of the project;

Reception and preparation of logistic equipment for the operation;





## PROJECTO SPD



### ACTIVITIES IN 2005

Change to new facilities and, consequently, the logistic re-adjustment concerning maintenance, stabilization, sustainability and physical security



## SPD PROJECT



### ACTIVITIES IN 2006

**Reception of the logistic equipment in lack, thus completing the ones in need;**

**Visit of evaluation team from European Commission between 30 January to 03 February. The objective of this evaluation was to aid the identification of issues which could affect the normal development of the project;**



## SPD PROJECT



### ACTIVITIES IN 2006

**Meeting with The Angolan Army Chief of Staff at his Headquarter, with participation of the Director, the Project Manager as well as the UNDP Programme Officer, the Evaluator of European Commission and other high rank entities of the FAA.**



## SPD PROJECT



### ACTIVITIES IN 2006

Analysis of the information and data collected about FAA AP stocked mines and those of campaign, as well as their mapped location. This analysis will allow us to elaborate a sounded Operational Plan for all the provinces, with particular incidence to Moxico and Kuando Kubango, in the third phase of the project;



## SPD PROJECT



### ACTIVITIES IN 2006

**To Elaborate the memorandum about the “Modus Operandis” of the Operational Teams to UNDP in order to be issued a certificate by the UN Security to the Advisor and the Assistents**



## SPD PROJECT



### **NATIONAL CAPACITY BUILDING**

20 FAA OFFICERS

02 NATIONAL POLICE OFFICERS

06 INSTRUCTORS FROM INAD



# SPD PROJECT



# SPD PROJECT



TRAINING AND NATIONAL CAPACITY BUILDING

SPD  
Course

Technical  
Survey  
Course

Reconversion Course  
Of Military Demining  
Into Humanitarian Demining

Demolition  
Course



## SPD PROJECT

### COURSE OF DISPOSAL OF EXPLOSIVE DEVICE AND AP MINES IN STOCK (STOCKPILE DISPOSAL)



## SPD PROJECT

### COURSE OF DISPOSAL OF EXPLOSIVE DEVICE AND AP MINES IN STOCK (STOCKPILE DISPOSAL)

To prepare the personnel of the project: Technical Assistants , personnel from FAA, INAD and National Police, for the performance of the training and field operations missions concerning the destruction of AP mines in stock and other explosive devices, both in the operational as well as the industrial technical context.

*As well as the fulfillment of the international agreements assumed by Angola, specifically the Ottawa Convention (art 4)*



## SPD PROJECT



### TECHNICAL SURVEY COURSE



## SPD PROJECT



### TECHNICAL SURVEY COURSE

To prepare the personnel to perform the missions of training and field operations concerning the Technical Survey, Marking of Mines, UXO and Ap mines and other Explosive Devices in stock hazard areas.



## SPD PROJECT



### COURSE OF RECONVERSION FROM MILITARY DEMINING INTO HUMANITARIAN DEMINING



## SPD PROJECT



### COURSE OF RECONVERSION FROM MILITARY DEMINING INTO HUMANITARIAN DEMINING

The Course of Requalification in Humanitarian Demining served to optimize the human resources in Angola, in other words to seize the opportunity to use “the Manpower” from the Armed Force for the development in a humanitarian perspective and framing acknowledged nationally and internationally.



## SPD PROJECT



### COURSE OF RECONVERSION OF MILITARY DEMINING INTO HUMANITARIAN DEMINING

To prepare the personnel particularly from FAA to perform the training and field operations missions concerning the standards of humanitarian standards.



## SPD PROJECT



### OBJECTIVES TO BE ACHIEVED IN 2006

1. TO FINISH THE TRAINING, NATIONAL CAPACITY BUILDING;
2. COMPLETION OF THE 3RD PHASE OF THE PROJECT UNTIL AGO06;
3. INCLUSION OF THE 4TH PHASE OF THE PROJECT UNTIL SET06;
4. COMPLETION OF THE 5TH PHASE, IF POSSIBLE, UNTIL DEZ2006





## SPD PROJECT



### CONSTRAINTS

1. FIVE MONTHS DELAY IN THE BEGINNING OF THE PROJECT (DONOR AND UN SYSTEMS);
2. DELAY IN THE RECEPTION OF IMPORTED EQUIPMENT;
3. STOCKED AP MINES IN AREAS DENSELY MINED;
4. ISSUE OF CREDENTIALS TO THE OPERATIONAL TEAMS



## SPD PROJECT



### RECOMMENDATION/PROPOSAL

**DUE TO THE PRESENTED FOREGOING CONSTRAINTS, SPECIALLY CONCERNING**

- >LENGTH OF THE COUNTRY.**
- >LONG PERIOD OF CIVIL WAR WITH MANY ACTORS NOT INVOLVED IN THE PROCESS.**
- >THE STOCKED AP IN AREAS DENSELY MINED AND WITH DIFFICULT ACCESS, BE UNDER CONSIDERATION**

**THE HYPOTHESIS OF A SHORT EXTENSION PERIOD OF THE TERM DEADLINE TIME FOR ANGOLA TO FULFIL THE ARTICLE 4 OF OTTAWA CONVENTION ON 31 DECEMBER 2006**



 **SPD PROJECT** 



A group of military personnel and officials are gathered outdoors for a meeting or briefing. A man in a military uniform stands on the left, holding a document and pointing towards a large board on an easel. A line of soldiers in camouflage uniforms stands in the background. On the right, several men in civilian clothing are seated on chairs, listening to the speaker. The scene is set under a large tree in an open, dusty area.



## SPD PROJECT



THE END

