

National Mine Action Authority Republic of South Sudan


Individualised Approach

Remaining Hazardous Areas in South Sudan as of 31 August 2022



UNMAS

Situation Mapped by
Number of Clearance Tasks per Payam

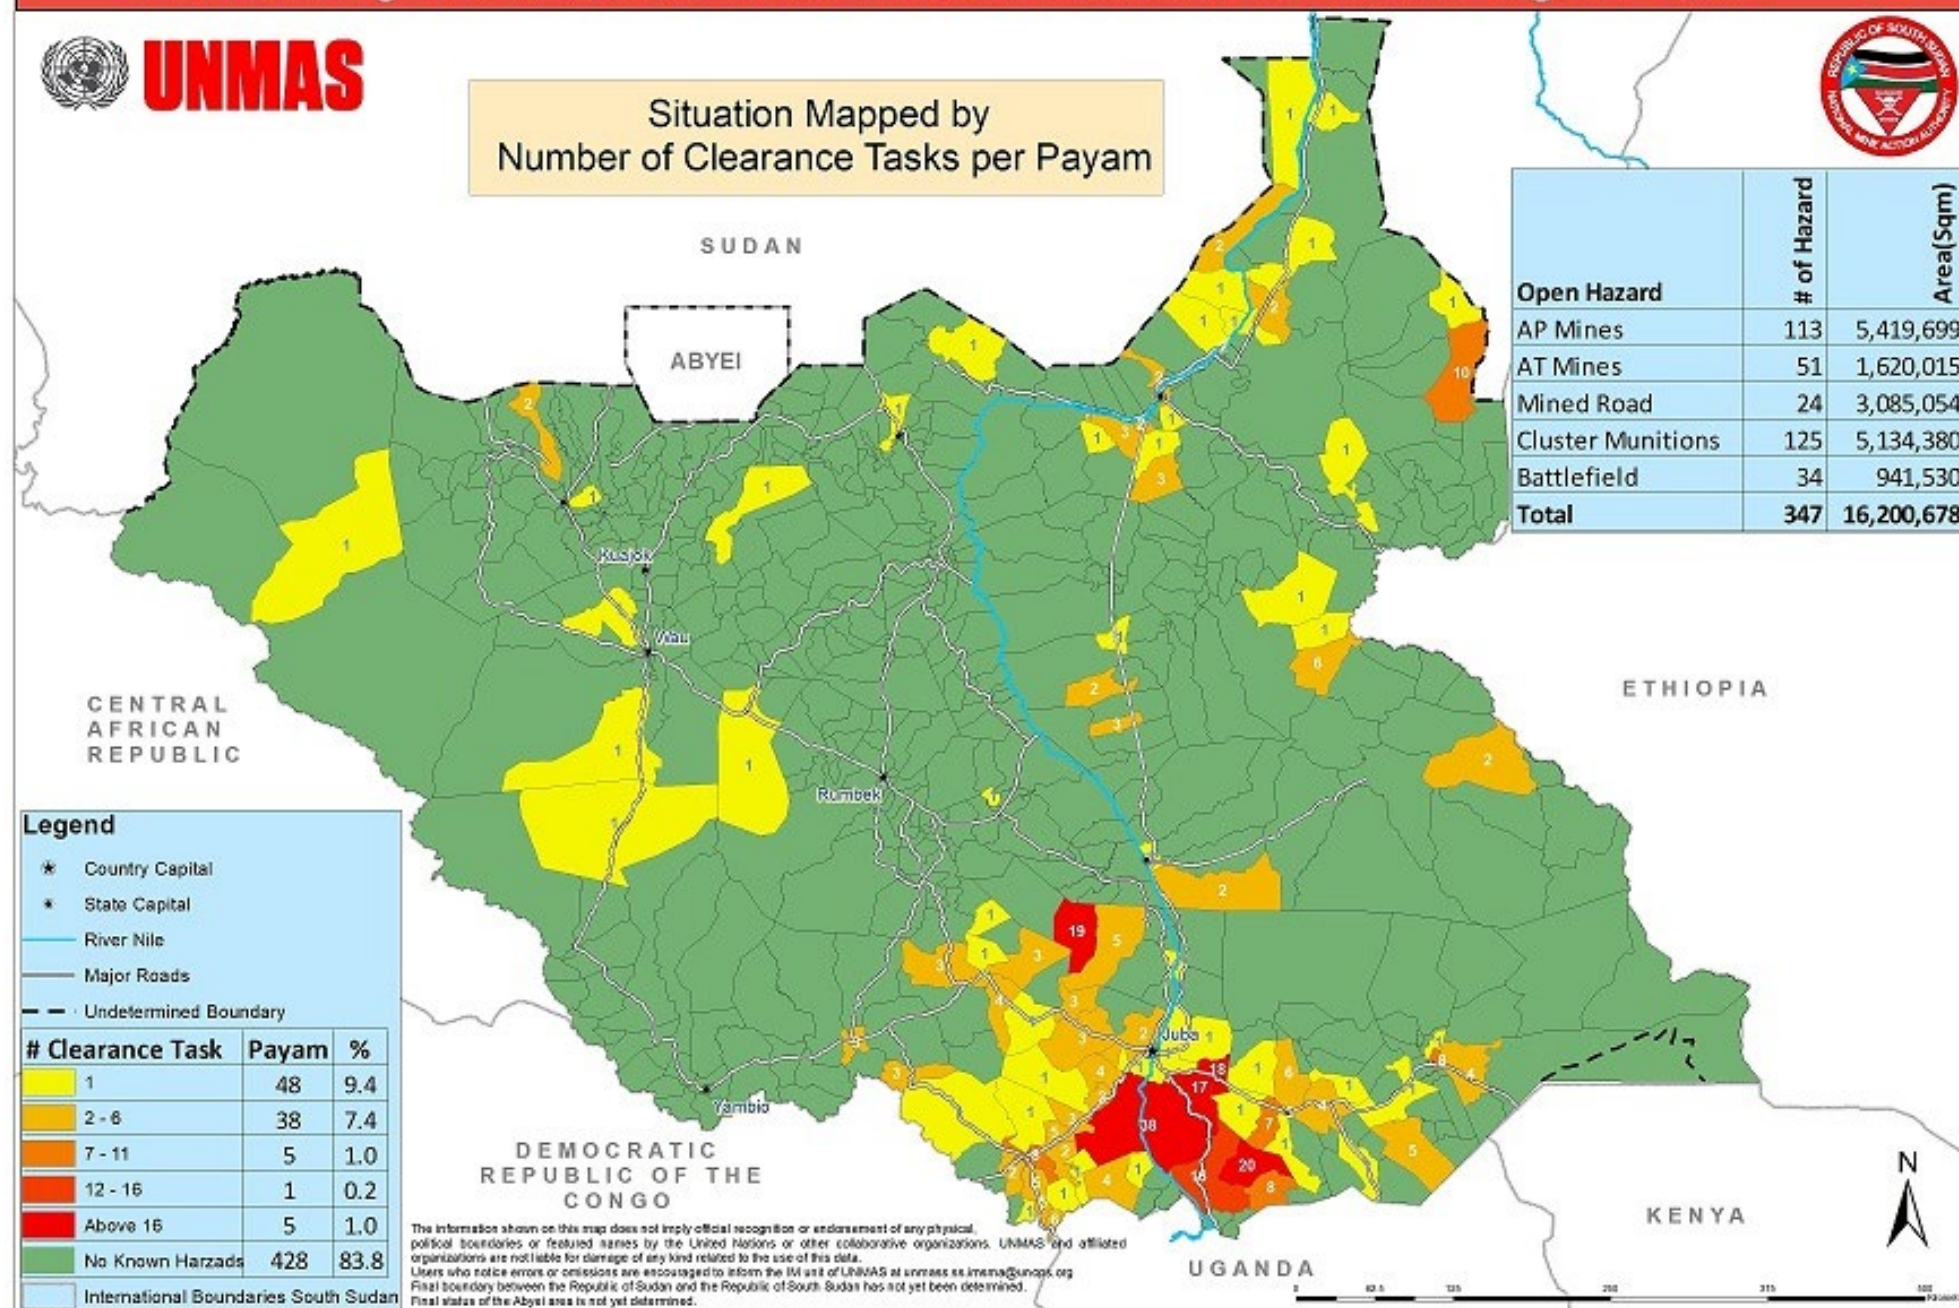

Remaining AP threat from July 2022

Remaining Anti-personnel mines threat	State	# of known AP-mines HAs	m2 of known AP-mines HAs	# of suspected AP-mines HAs	m2 of suspected AP-mines HAs	Total AP-mines HAs m2	Estimated date of completion (year-end)	Average per HA
1	Central Equatoria	38	1,340,711	28	224,819	1,565,530	2026	23,720
2	Eastern Equatoria	17	804,064	5	41,836	845,900	2025	38,450
3	Jonglei	3	208,802	8	1,656,580	1,865,382	2026	169,580
4	Northern Bahr El Ghazal	2	83,384	0	0	83,384	2023	41,692
5	Upper Nile & Unity	4	318,543	0	0	318,543	2024	79,636
6	Warrap & Lakes	0	0	1	40,000	40,000	2022	40,000
7	Western Bahr El Ghazal	1	201,738	0	0	201,738	2023	201,738
8	Western Equatoria	1	99,398	5	399,824	499,222	2024	83,204
TOTAL		66	3,056,640	47	2,363,059	5,419,699		

Circumstances Impeding Completion



The greatest risk to this funding plan is a return to violence. The international community are already supporting the country with more than \$ 2 billion dollars of assistance per year and is struggling to cope with the needs of six million people displaced, widespread flooding, the ongoing inter-communal violence that primarily revolved around grazing rights and cattle migration – and the political violence that has fluctuated for the last six years from underlying tensions to outright war. Funding mine action thus is often relegated down the list of donor priorities.

Institutions responding to the remaining challenge

- South Sudan National Mine Action Authority (NMAA).
- Mine Action activities are currently coordinated jointly by the NMAA and UNMAS.
- UNMAS currently contracts 3 commercial companies (19 demining teams) to support UNMISS and their mandate.
- 3 International Non-Governmental Organisations deploy further 11 teams.
- 1 national NGO team - inconsistent funding.
- 7 national EORE organisations.



Current cooperation and assistance / Challenges



Current cooperation and assistance / Challenges

Capacity estimated to be required to complete milestone

Team Type	Required number of teams				
	2022	2023	2024	2025	2026
15 x deminers Manual Teams	16	16	10	10	5
BAC - Cluster-munitions strikes	4	4	4	3	0
Mechanical	2	4	3	3	3
Road Clearance	4	4	4	0	0
Survey/EOD	4	4	4	4	4

- ❖ The shortfall is in mechanical clearance assets, and UNMAS plans to deploy 3 x mechanical teams from October 2023 until June 2026. With one additional mechanical team deployed by DCA, areas requiring mechanical assistance could be addressed by June 2026.





Expected Milestones

		CEQ	EEQ	Jonglei	North BGZ	Upper Nile & Unity	Warrap & Lakes	Western Equatoria	West BGZ	TOTAL AP m/f
2020	#	4	3	0	3	2	0	0	0	12
	m2	382,853	323,006	133,207	56,875	159,272	0	0	0	1,055,213
2021	#	9	2	0	0	0	0	1	0	12
	m2	277,085	7,350	0	5,420	0	0	8,986	0	298,841
2022	#	13	6	2	0	1	0	1	0	23
	m2	308,362	230,700	339,160	0	79,636	0	83,204	0	1,041,062
2023	#	15	5	3	1	1	1	3	1	30
	m2	355,802	192,250	508,741	41,692	79,636	40,000	249,611	201,738	1,669,470
2024	#	14	5	2	1	1	0	2	0	25
	m2	332,082	192,250	339,160	41,692	79,636	0	166,407	0	1,151,228
2025	#	13	4	2	0	1	0	0	0	20
	m2	308,362	153,800	339,160	0	79,636	0	0	0	880,958
2026	#	11	2	2	0	0	0	0	0	15
	m2	260,922	76,900	339,160	0	0	0	0	0	676,982
	#	66	22	11	2	4	1	6	1	113
	m2	1,565,530	845,900	1,865,382	83,384	318,543	40,000	499,222	201,738	5,419,699

Follow up Activities

- NMAA to coordinate with UNMAS UNMISS and organise Mine Action Workshop, with relevant stakeholders, aimed at defining actions needed to redefine the contamination problem and ensure continuation of funding of mine action activities in the country.
- NMAA to coordinate with UNMAS UNMISS and organise donor round table conferences, to identify supporters that would provide funding to mine action programme in the country.





END
