



**KINGDOM OF CAMBODIA**  
**Nation Religion King**

**Presentation of Extension Request**  
**International Conference Centre Geneva (CICG)**  
**SWITZERLAND**

**17-20 June 2025**








# Progress of the previous extension period

**01 January 2020 to 31 December 2024:**

## Progress:

- Released **884,294,412** square meters of land contaminated by anti-personnel mines through NTS (16%), TS (30%), and clearance (54%).


**Planned area VS Actual area  
for Land Release 2020-2024**

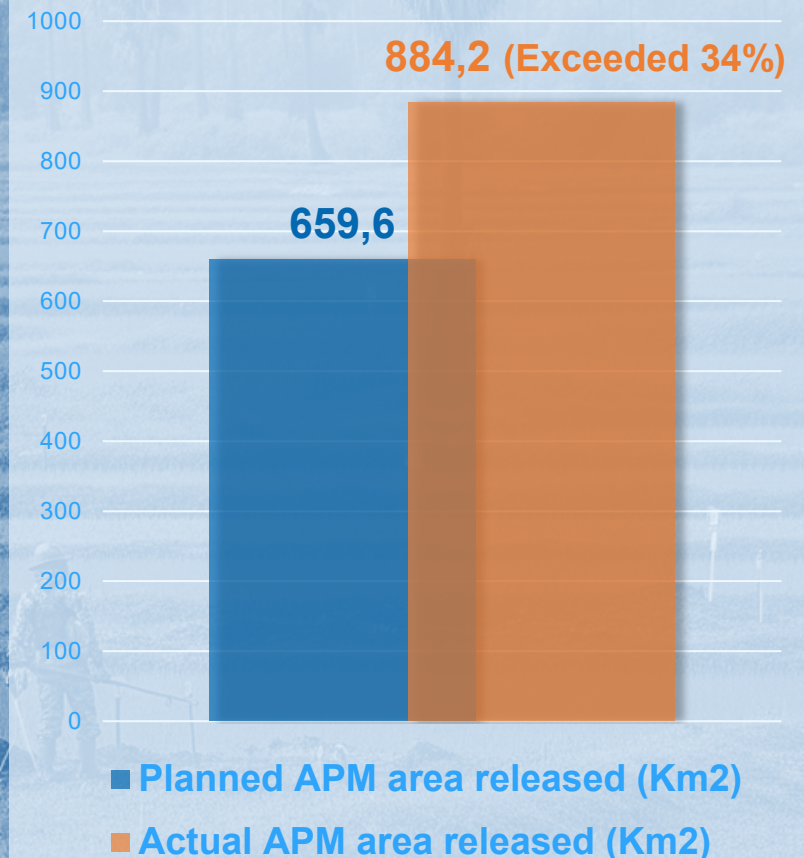







# Progress of the previous extension period



USD 307 M required but  
USD 268 M actually  
mobilized


## 15 mine-free provinces

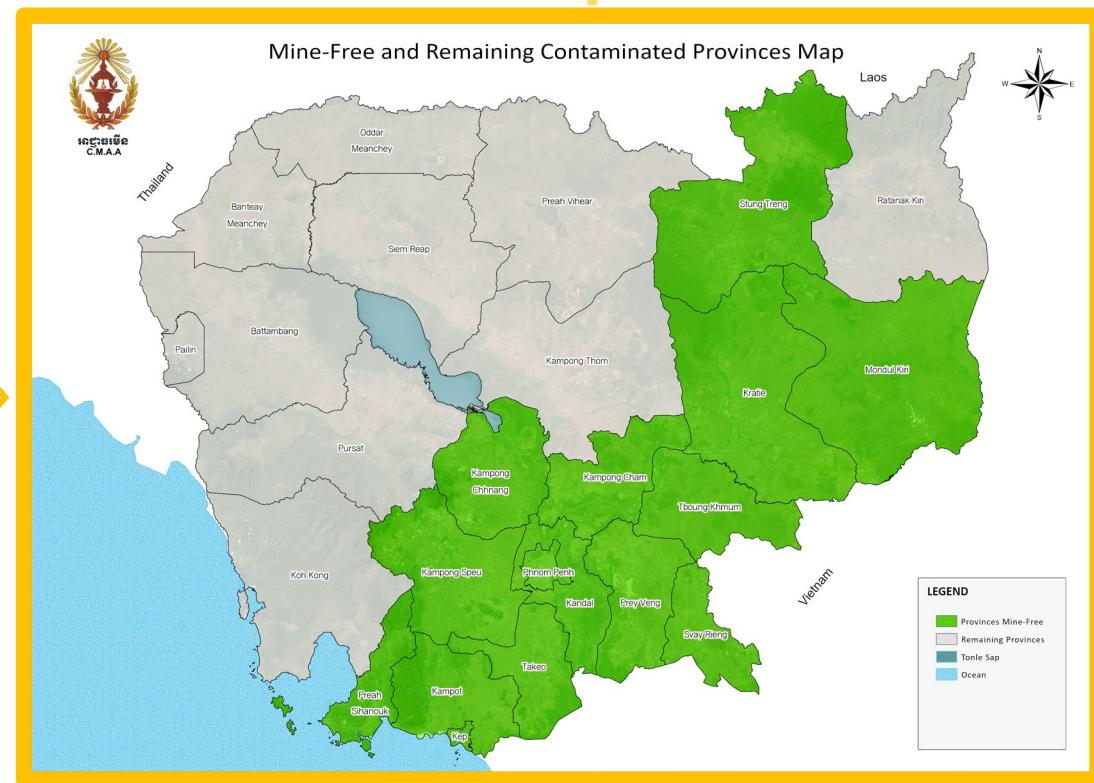




# Reasons for not completing obligations during the previous extension period


## CHALLENGES:



- Shortfall in funding due to the COVID-19 global impact and international funding priority shifting.
- The magnitude of the remaining problem

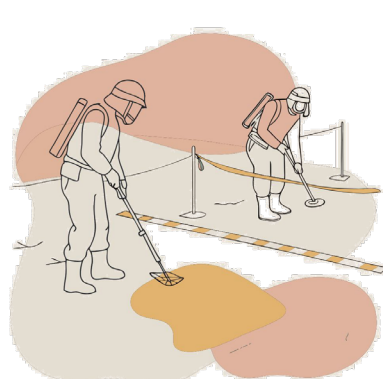


- Needs to address other types of ERW contamination, namely anti-tank mines, cluster munitions, UXO, underwater contamination, and aerial bombs.



- **Discovery of new minefields:** 49% of mine accidents over the past decade (2015–2024) occurred outside the recorded minefields,



- Geographical Challenges: Landmine clearance has moved to more challenging minefields located in rugged mountainous terrain and dense forests, making access extremely difficult.

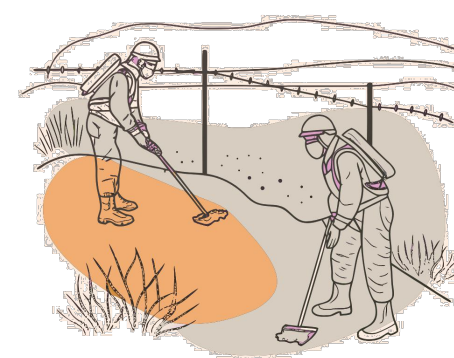


- Border Challenges: Challenges along the border between Cambodia and Thailand, including incomplete demarcation, hinder the clearance of minefields in this area.





# Current remaining challenges

- Cambodia still has **424,238,236** square meters of land contaminated by anti-personnel mines on the national database.
- A comprehensive survey is underway and is expected to be completed by the end of June 2025.
- The survey is expected to add additional challenges.

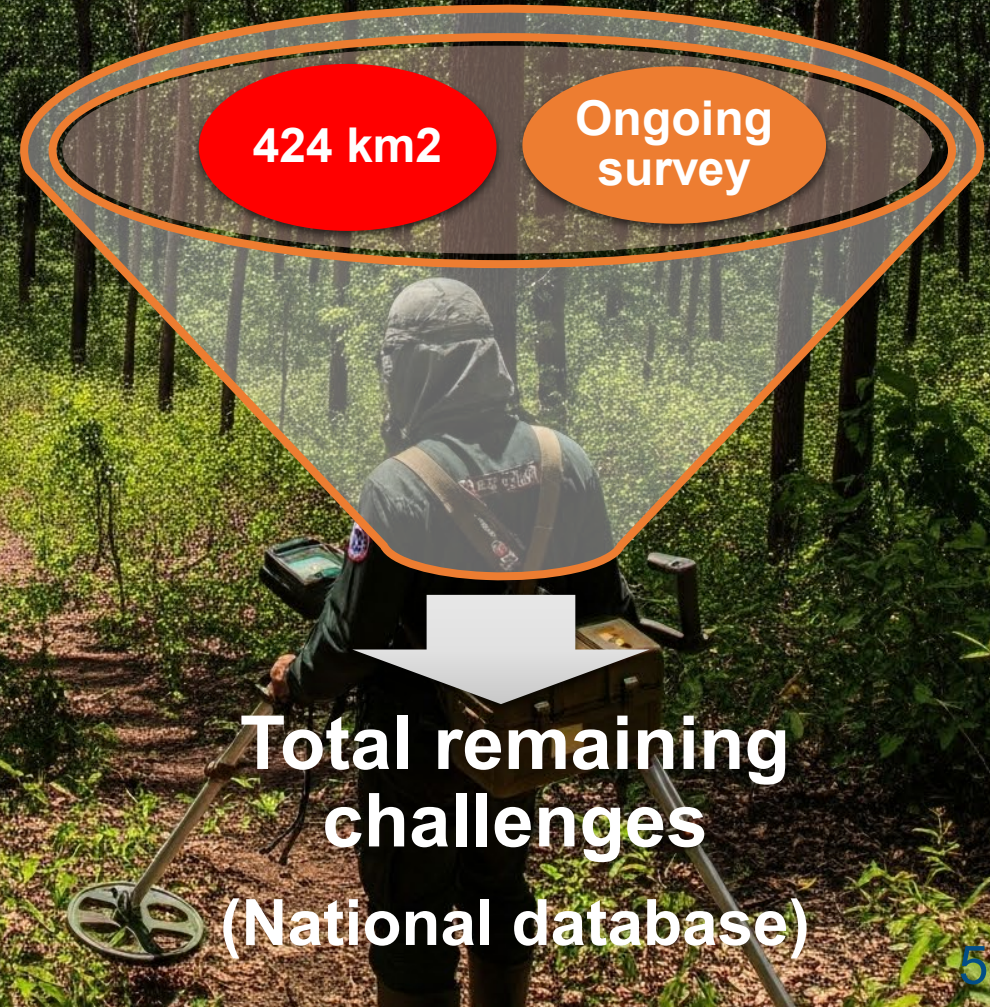







# Requested extension duration and justification for the time needed

- Cambodia seeks a five-year extension until 2030 based on the magnitude of the remaining challenges and the additional challenges to be identified by the comprehensive survey.
- The results of the survey will enable Cambodia to fully understand the magnitude of the remaining challenges and update the current provisional work plan.

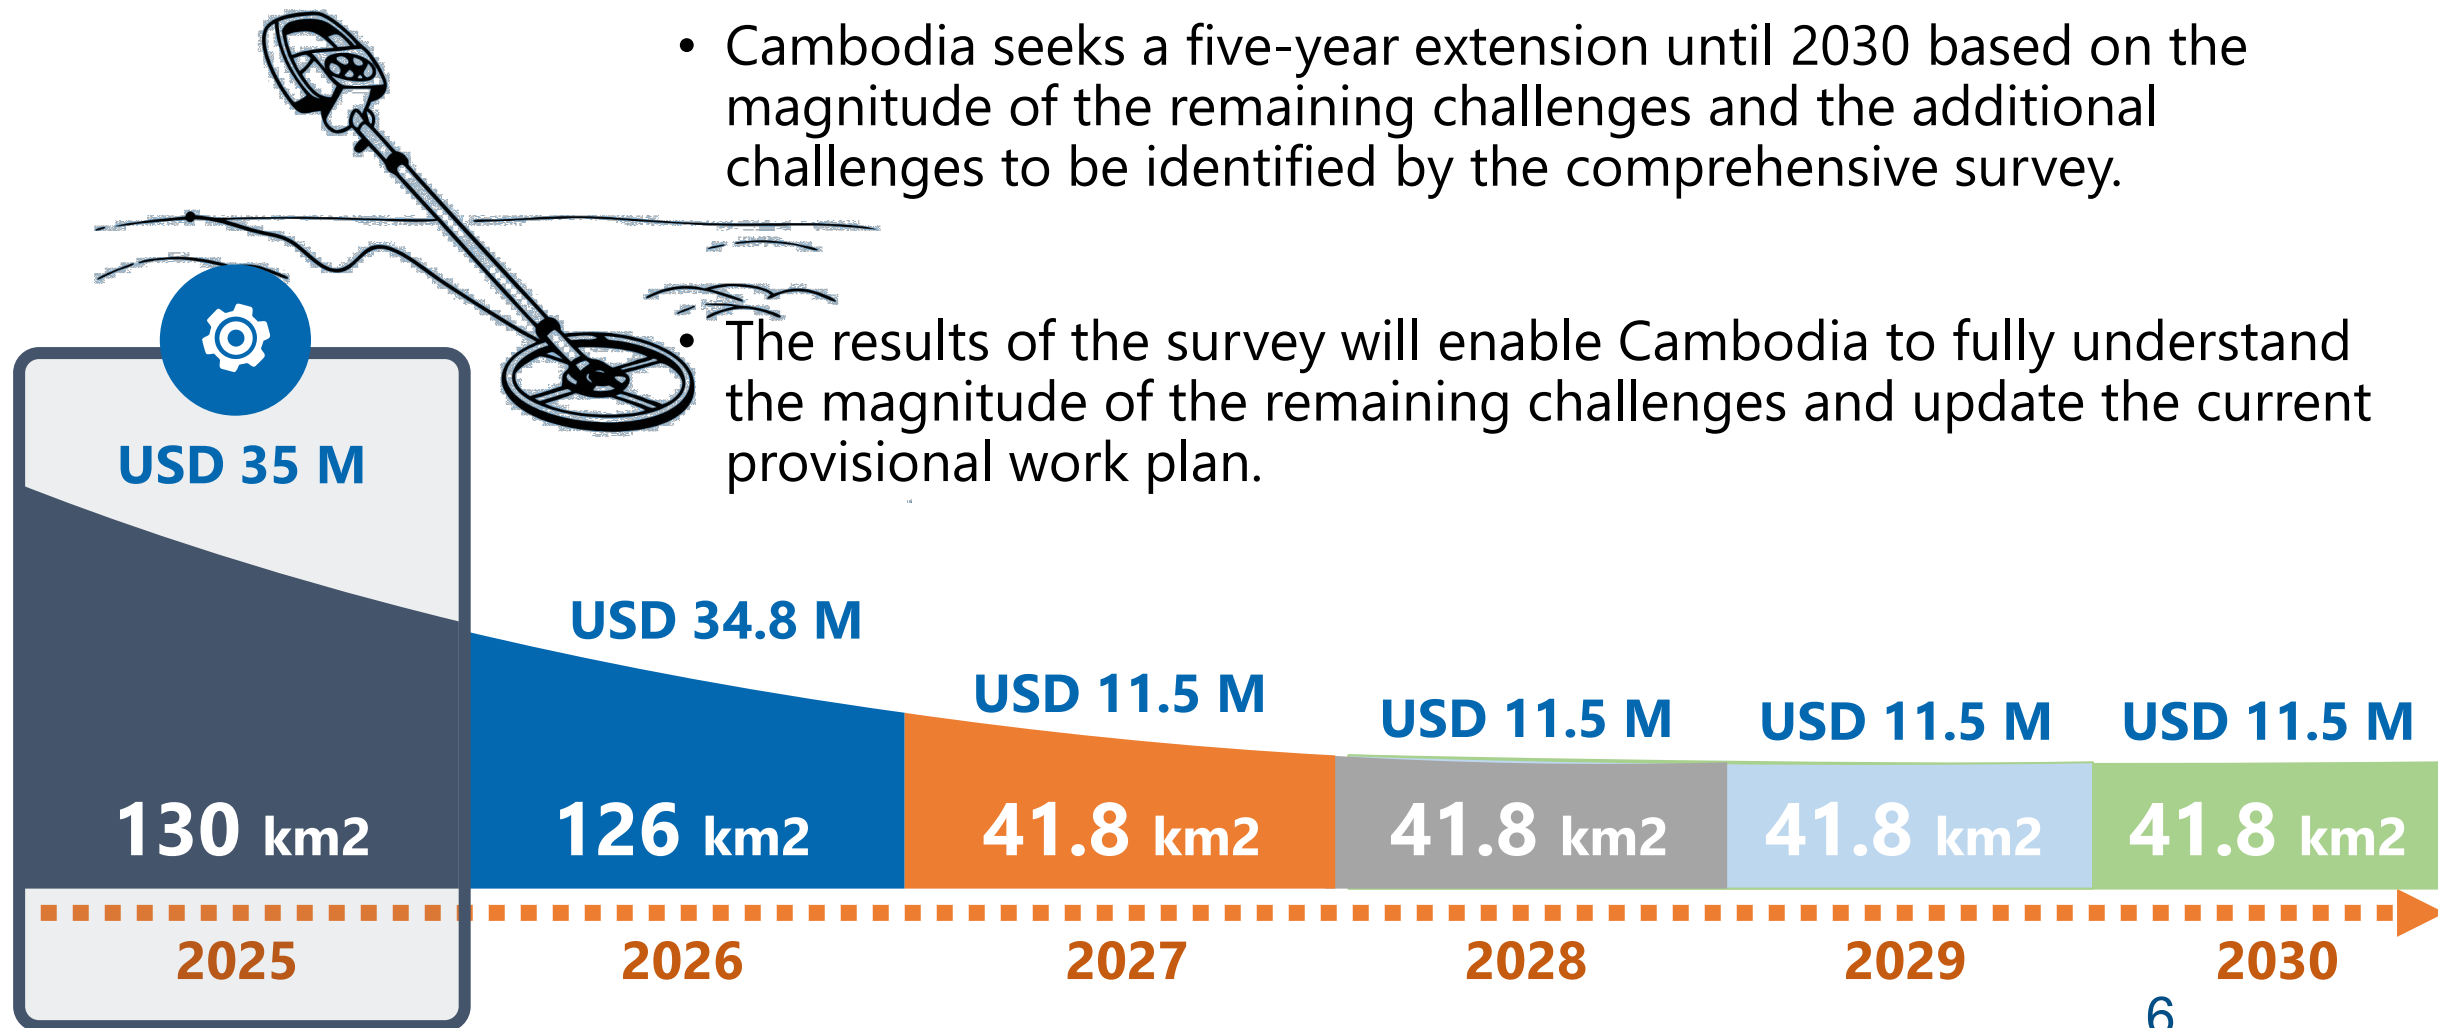



# Planned activities during the extension period

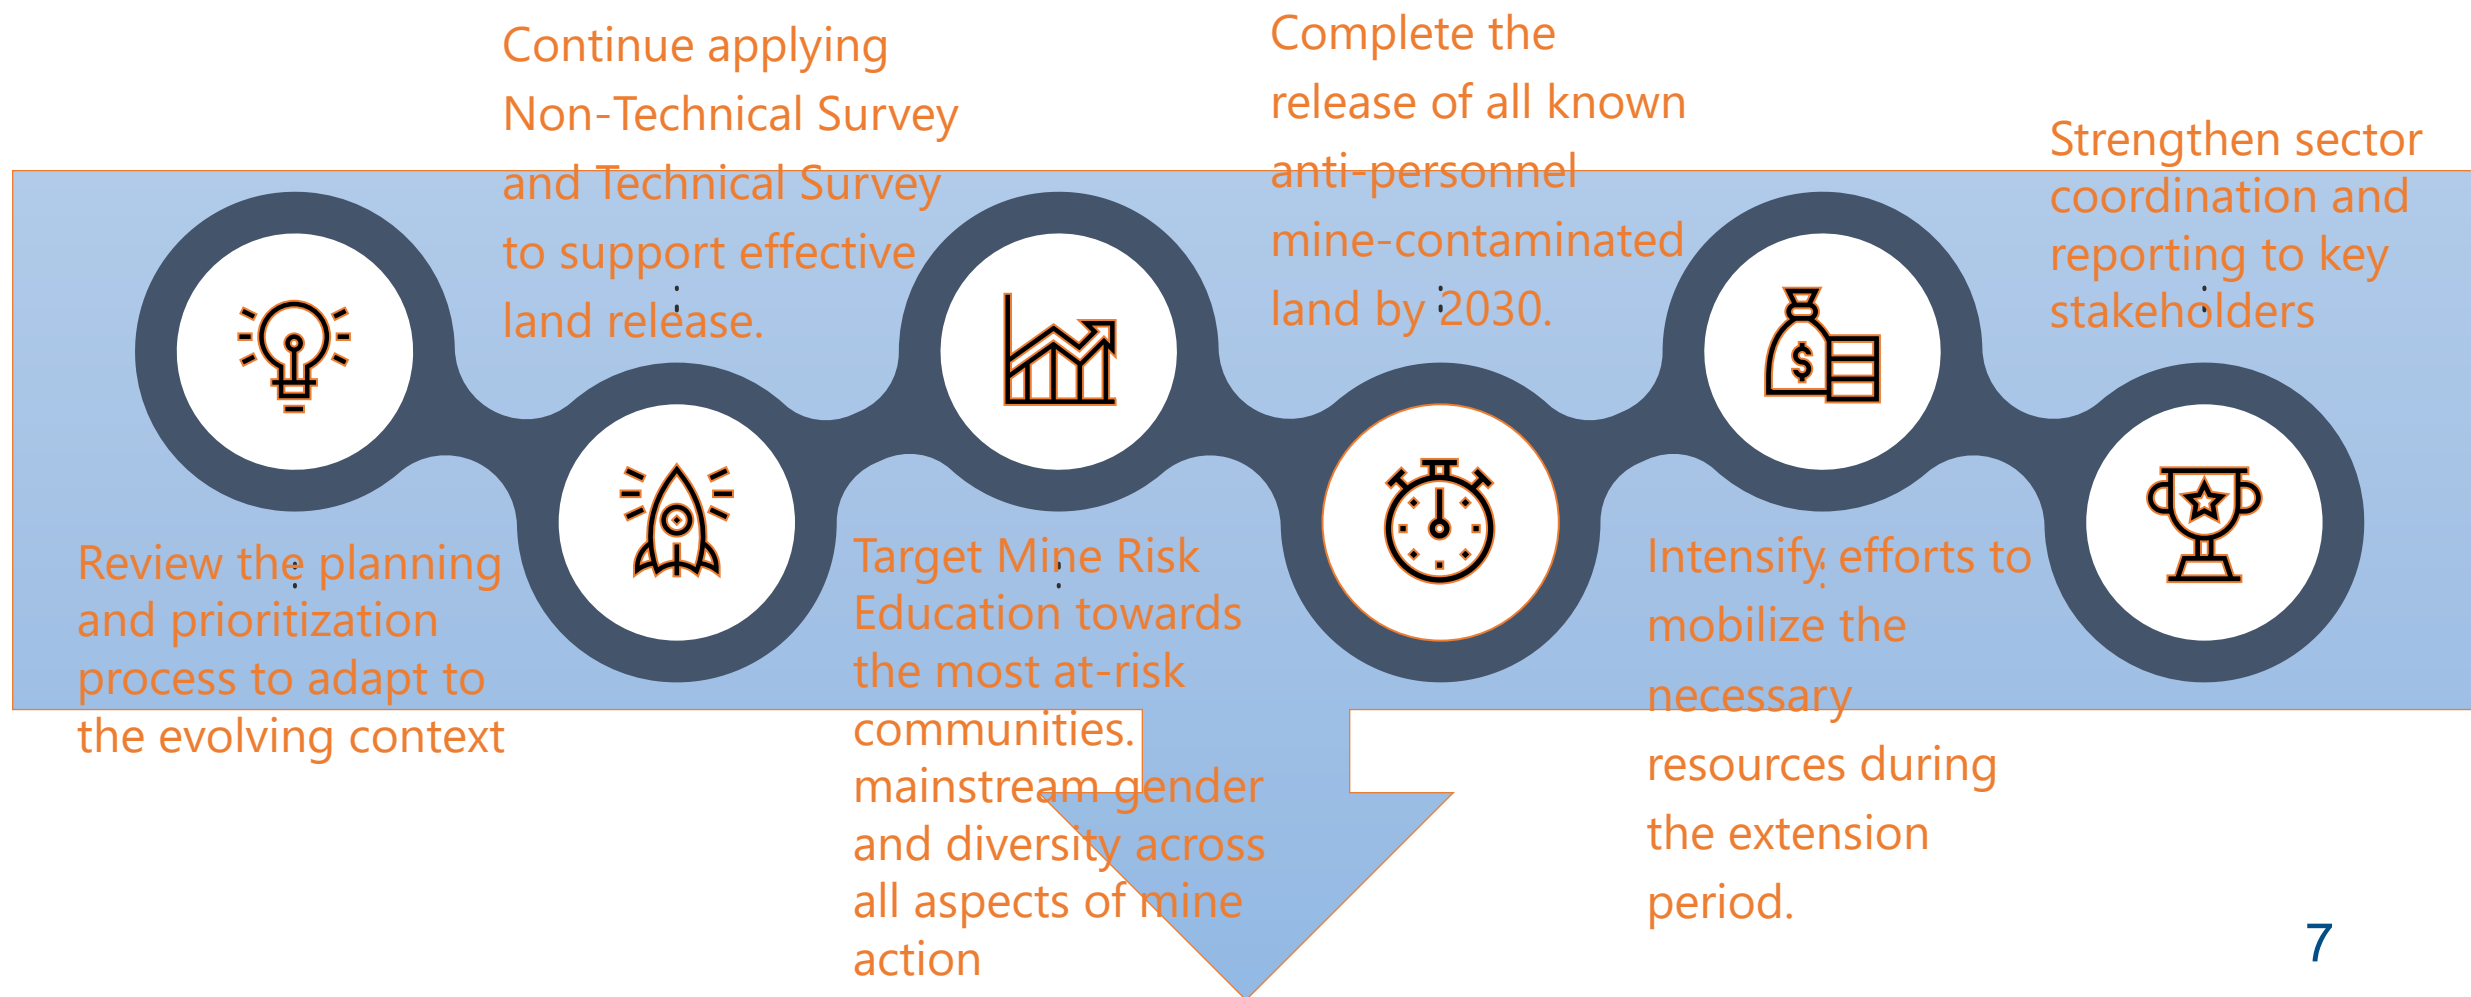

**The planned activities for implementation for the period 2026-2030**



# Assistance required to achieve completion

Cambodia requires **US\$ 116,988,192**, subject to recalculation based on the updated anti-personnel mine contamination data after completing the comprehensive survey by June 2025, to address the challenges in the national database during this 5-year extension period.

*Progress made during the 2<sup>nd</sup> ER 2020-2024*

Planned APM area released = **659.6 km<sup>2</sup>**  
The actual APM area released = **884.2 km<sup>2</sup>**  
(Exceeded 34%)



**2025**



*3rd ER 2026 2030*



**Budget  
Requirement  
USD 116 M**

**Remaining challenges**

**424 km<sup>2</sup> + additional contamination**  
(ongoing survey)





សូមអរគុណ!

Thank you!

BM

បង្គោលចម្លង  
ការប្រមូលសម្ភារៈ
