






PRESENTATION ON ZIMBABWE'S ARTICLE 5 EXTENSION REQUEST


08 JUNE 2017

BY
COL MB NCUBE
DIRECTOR ZIMBABWE MINE
ACTION CENTRE

BACKGROUND

MINEFIELDS IN ZIMBABWE UPDATE AS AT 31 MAY 2017

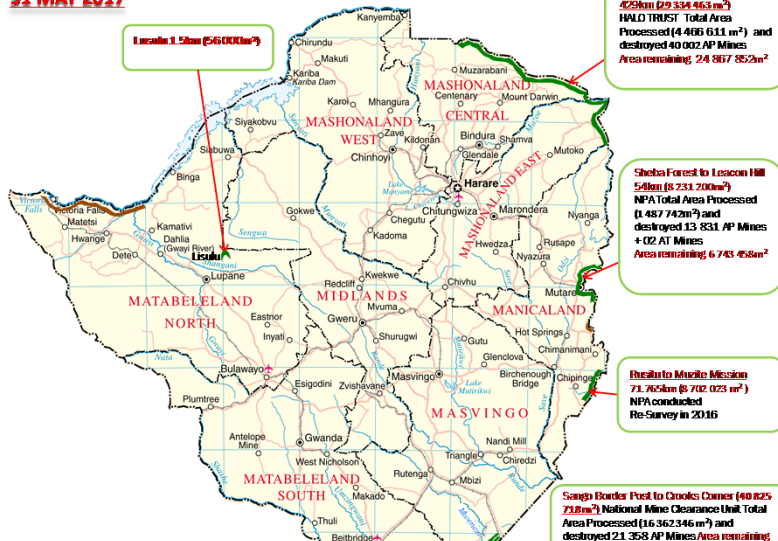

- Local 1.5km (56000m²)**
- Muzarabani to Pirovya River 409km (29 334 463 m²) HALO TRUST Total Area Processed (4 486 611 m²) and destroyed 40 002 AP Mines Area remaining: 24 867 852m²**
- Shoko Forest to Lason Hill 54km (8 231 200m²) NFA Total Area Processed (1 487 742m²) and destroyed 13 831 AP Mines + 02 AT Mines Area remaining: 6 743 458m²**
- Bheala to Muzila Mission 71.765km (8 702 023 m²) NFA conducted Re-Survey in 2016**
- Sango Border Post to Crooks Corner (40 km² 23,8km²) National Mines Clearance Unit Total Area Processed (16 362 346 m²) and destroyed 21 358 AP Mines Area remaining: 24 463 372 m²**




REQUESTED PERIOD OF EXTENSION

Zimbabwe now seeks an eight (8) year extension period, January 2018 to December 2025.










Table 1: Contamination Level as at June 2014

	Mined Areas	Total Area (m²)
1	Musengezi to Rwenya	29 327 211
2	Sango Border Post to Crooks Corner	28 605 729
3	Rusitu to Muzite Mission	8 702 023
4	Sheba Forest to Leacon Hill	8,231 200
5	Lusulu	56,000
	TOTAL	74 922 163

 Table 2: Contamination Level as at 31 May 2017 		
Mined Area	Area (m ²)	Organisation
1 Musengezi to Mazowe River	13 590 152	HALO Trust
2 Mazowe River to Rwenya River	11 277 700	MAG
3 Sango Border Post to Mwenezi River	17 281 734	National Mine Clearance Unit
4 Sango Border Post to Mwenezi River	7 181 638	APOPO
5 Rusitu to Muzite Mission	8 702 023	NPA
6 Sheba Forest to Leacon Hill	6 743 458	NPA
7 Lusulu	56,000	National Mine Clearance Unit
8 TOTAL	64 832 705	

 Table 3: Annual Projected Clearance Plan (m²) 2017 – 2025 										
Minefield	2017	2018	2019	2020	2021	2022	2023	2024	2025	TOTAL
Musengezi to Mazowe (HALO)	441,720	1,405,700	1,740,000	1,740,000	1,740,000	1,740,000	1,740,000	1,740,000	1,302,732	13,590,152
Mazowe to Rwenya River (MAG)	700,000	802,000	1,100,000	1,300,000	1,500,000	1,600,000	1,650,000	1,650,000	975,602	11,277,700
Crooks Corner to Sango Border (NMC)	2,089,636	2,100,000	2,100,000	2,100,000	2,100,000	1,900,000	1,900,000	2,000,000	992,098	17,281,734
Crooks Corner to Sango Border (APOPO)	300,000	900,000	750,000	900,000	850,000	900,000	1,000,000	800,050	781,588	7,181,638
Rusitu to Muzite Mission (NPA)	164,104	984,000	1,000,000	1,200,000	1,500,000	1,600,000	1,600,000	653,919		8,702,023
Sheba Forest to Leacon Hill (NPA)	1,355,360	1,810,000	1,810,000	1,768,098						6,743,458
Lusulu (NMC)					30,000	26,000				56,000
Total	5,050,820	8,001,700	8,500,098	9,008,098	7,720,000	7,766,000	7,890,000	6,843,969	4,052,020	64,832,705






Table 4: Projected Funding 2017-2025

Organisation	Year										Total
	2017	2018	2019	2020	2021	2022	2023	2024	2025		
International Donor / Operational Support											
NPA	3	3.15	3.3	3.46	3.63	3.81	4	4.2	4.41	32.96	
HALO	4.65	5.36	5.25	5.69	5.8	6.03	6.21	6.4	6.59	45.39	
APOPO	1	2	2	2	3.4	3.5	3.4	2.4	2	21.7	
MAG	0.7	1	1	1.5	1.5	3	3	3	3	17.7	
Sub-Total	9.35	11.51	11.55	12.65	14.33	16.34	16.61	16	9.41	117.75	
Zimbabwe Government Support											
NMCU	0.6	0.7	0.9	1	1	1.5	2	2.5	2.5	12.7	
Total	9.95	12.21	12	13.65	15.33	17.84	18.61	18.5	11.91	130.45	

- 
- 
- ❖ Low accidents rates among civilians.
 - ❖ Low security risks in country for operations.
 - ❖ High impact of cleared land for socio-economic development.
 - ❖ Areas and size of contamination is known with a clear plan, known capacities and resources to achieve these obligations.
