



Kingdom of Thailand

**Request for an extension of the
deadline for completing the
destruction of
anti-personnel mines in mined areas
in accordance with Article 5,
paragraph 1 of the Convention on the
Prohibition
of the Use, Stockpiling, Production
and Transfer of Anti-Personnel Mines
and on Their Destruction**



20MSP

Twentieth Meeting of the States Parties
21-25 November 2022, Geneva



Overall Progress in Thailand's Mine Action Efforts

Year	Remaining Mine Contaminated Areas in Thailand (sqm)	Remaining areas as percentage of the Initial Landmine Impact Survey
2001 : Initial Landmine Impact Survey	2,556,700,000	100 %
2008 : The end of the initial operation period	528,350,000	20.67 %



Thailand's Efforts and our International Partners

Japan



Norway




United States






20 Years of Learning and Development

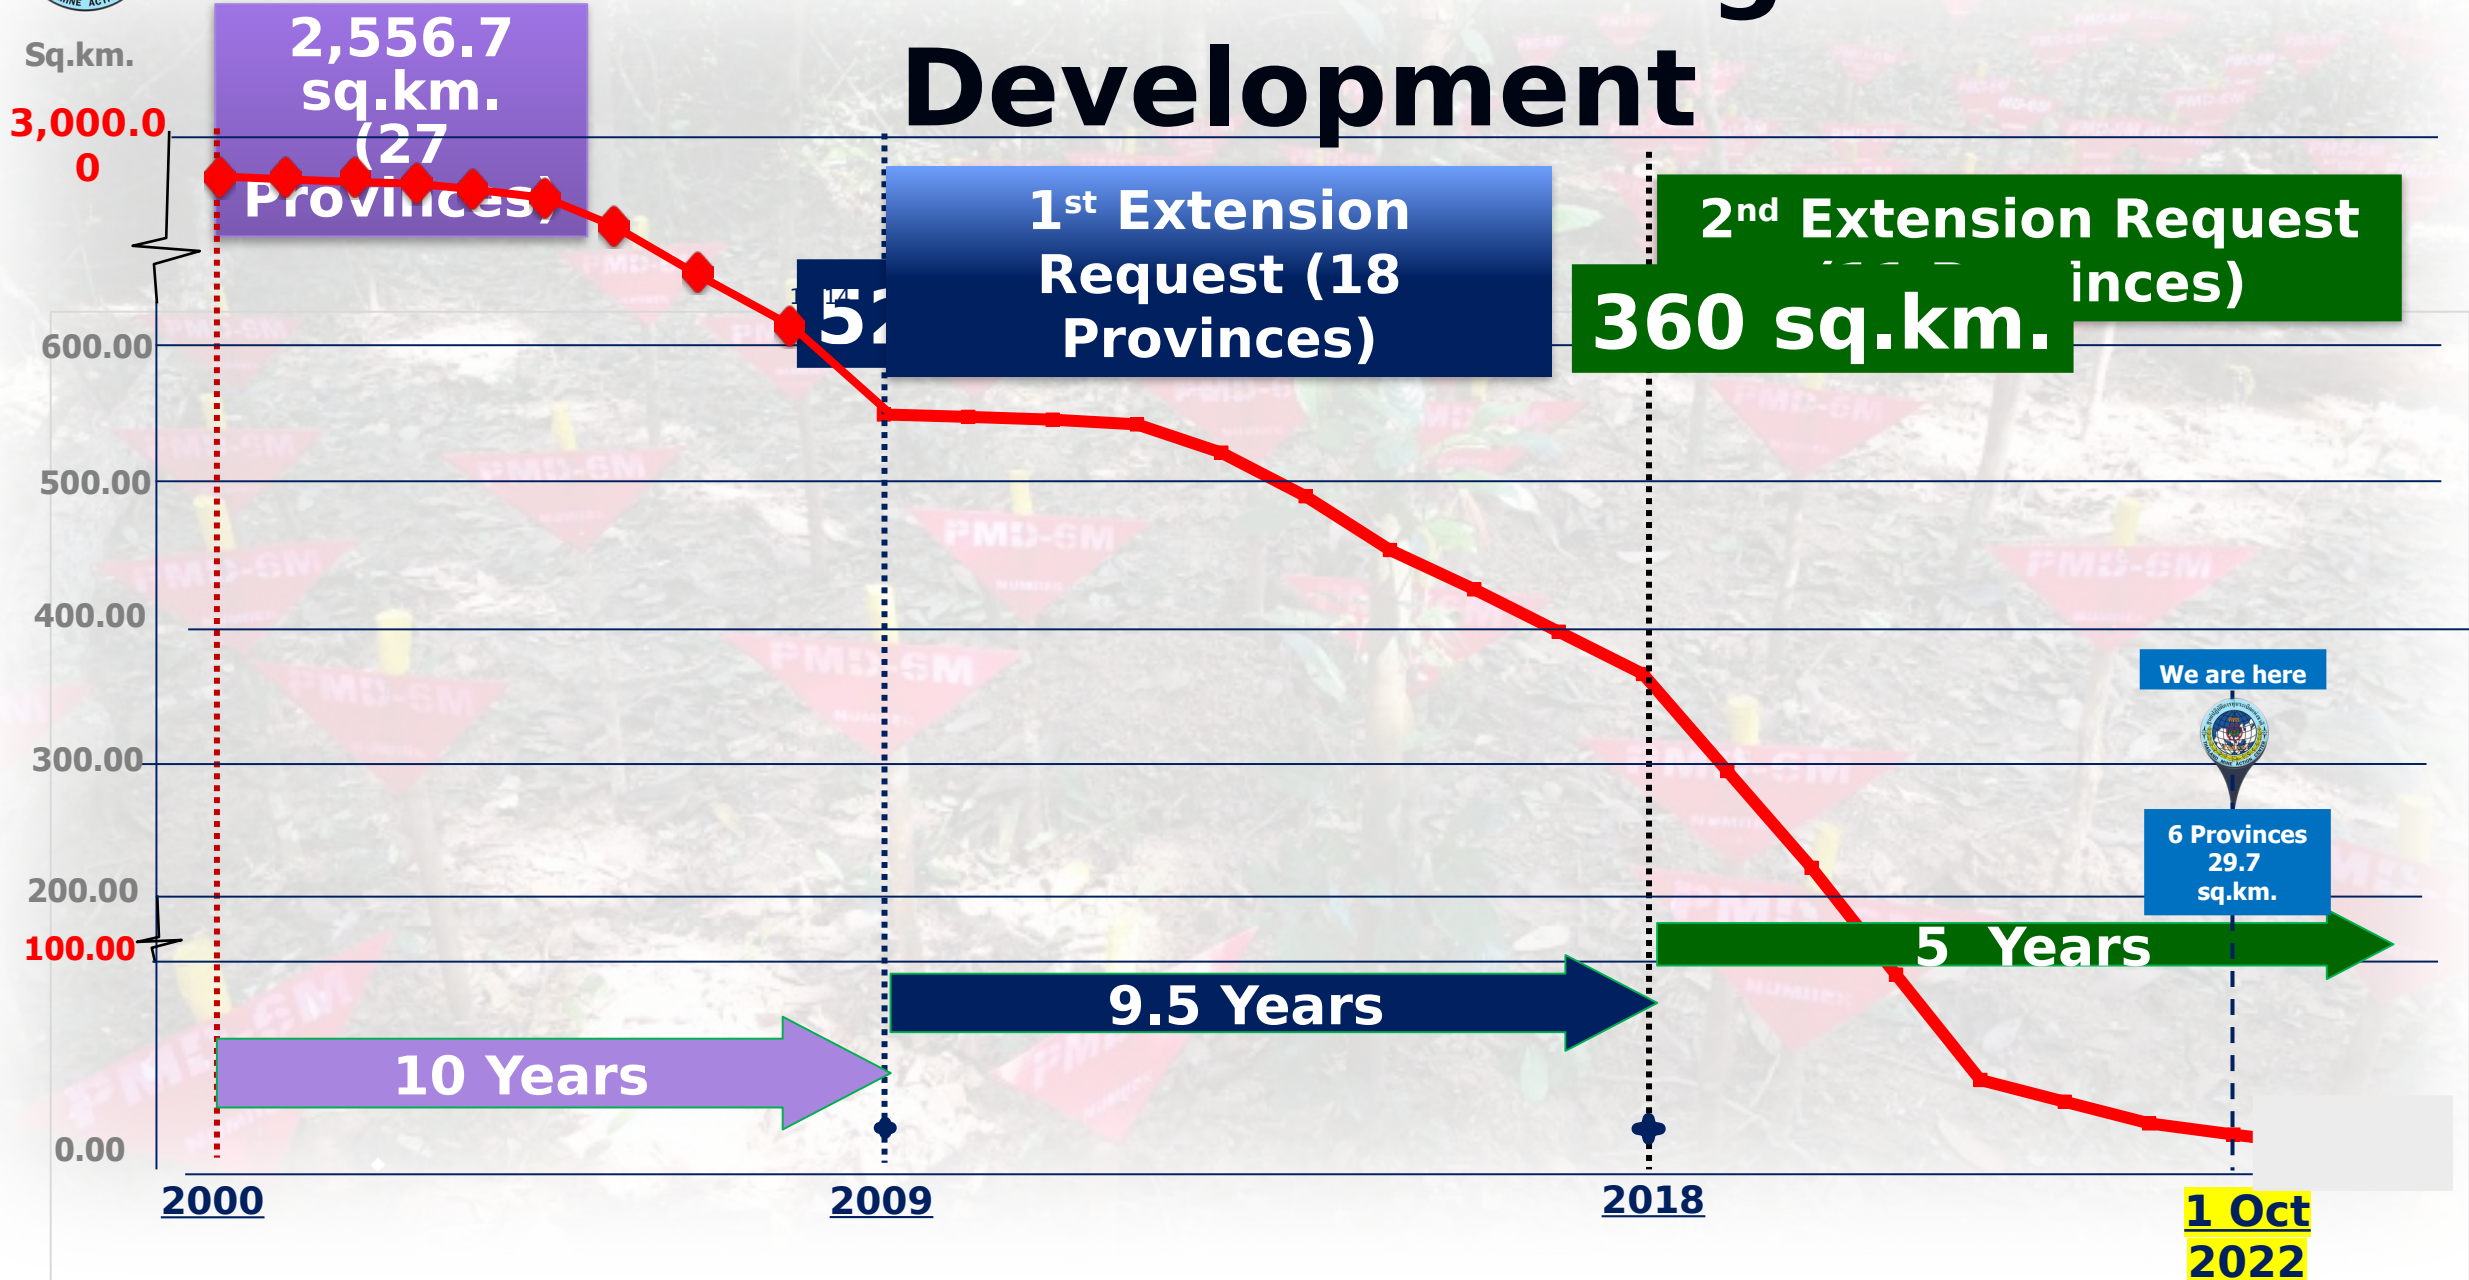



The Remaining Areas by Province

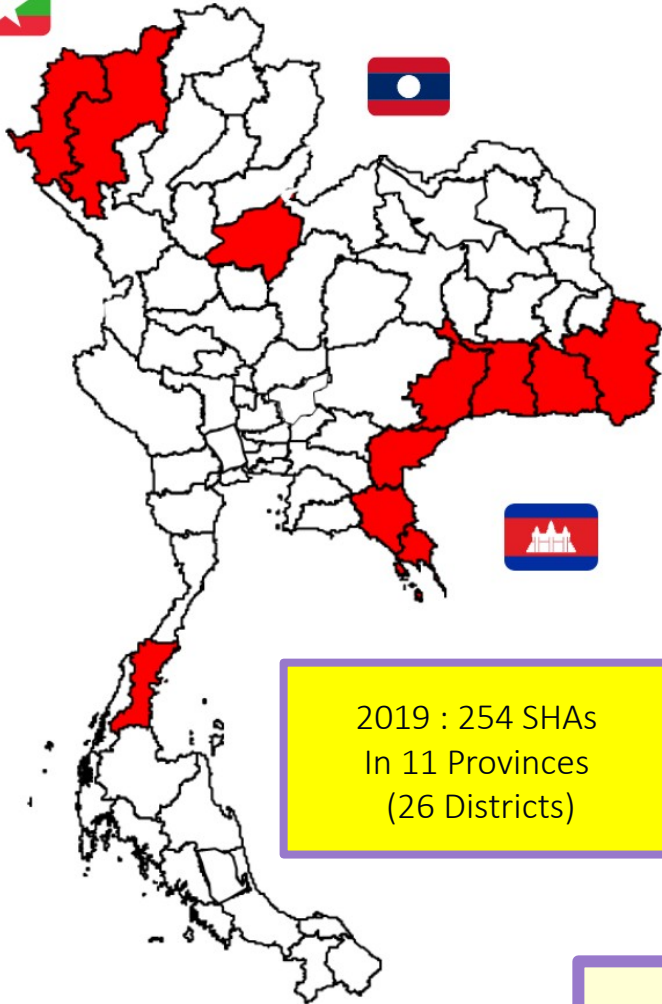


2019 : 254 SHAs
In 11 Provinces
(26 Districts)

2019 - 2023
Released 332.6
sq.km

Mine-Free : 5
Provinces
- Chiang Mai
- Mae Hong Son
- Chumphon
- Phitsanulok

44,992 anti-personnel mines and
3,049 UXOs were recovered and destroyed.

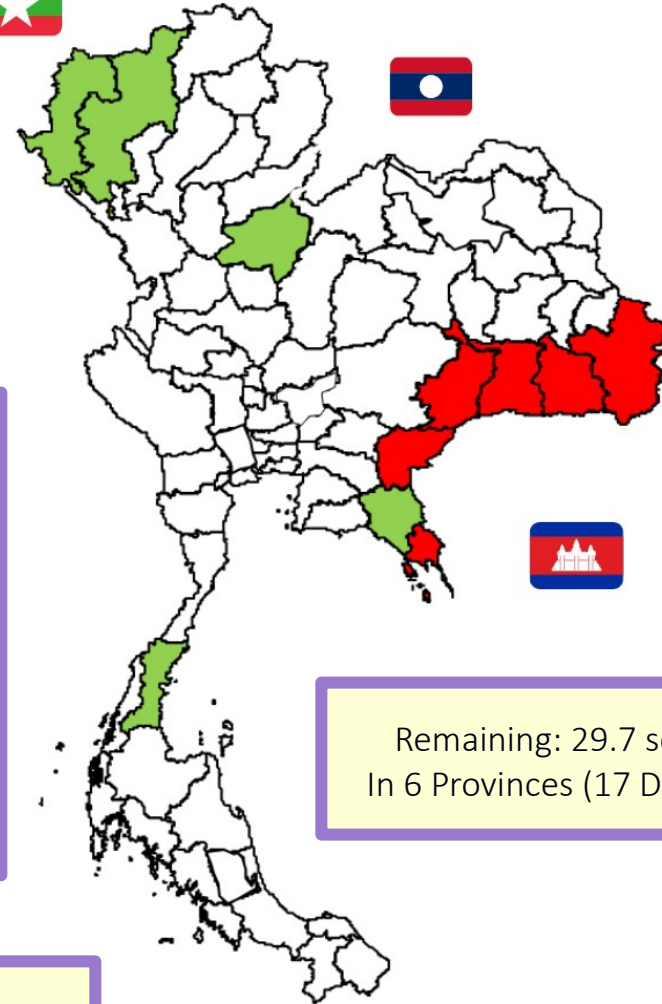

Remaining: 29.7 sq.km.
In 6 Provinces (17 Districts)



Factors that has led to Progress

- Execution of the Five-Year Work Plan
- Commitment towards Improvement of Information Management
- Commitment towards funding by the Royal Thai Government
- Strengthening International Cooperation at all levels



Updated Work Plan & Information Management



Five-Year Humanitarian Mine Action Plan

1 Nov 2018 – 31 Oct 2023


As of 15 March 2019



Thailand Mine Action Center

Policy and Plans Division of Thailand Mine Action Center, Songrapha Road, Sigon Subdistrict, Don Mueang District, Bangkok 10710 Thailand Tel: +66 2070 9191 Fax: +66 2070 9075 Website: www.thamc.org thamc@thamc.org

Updated 5-Year Work Plan

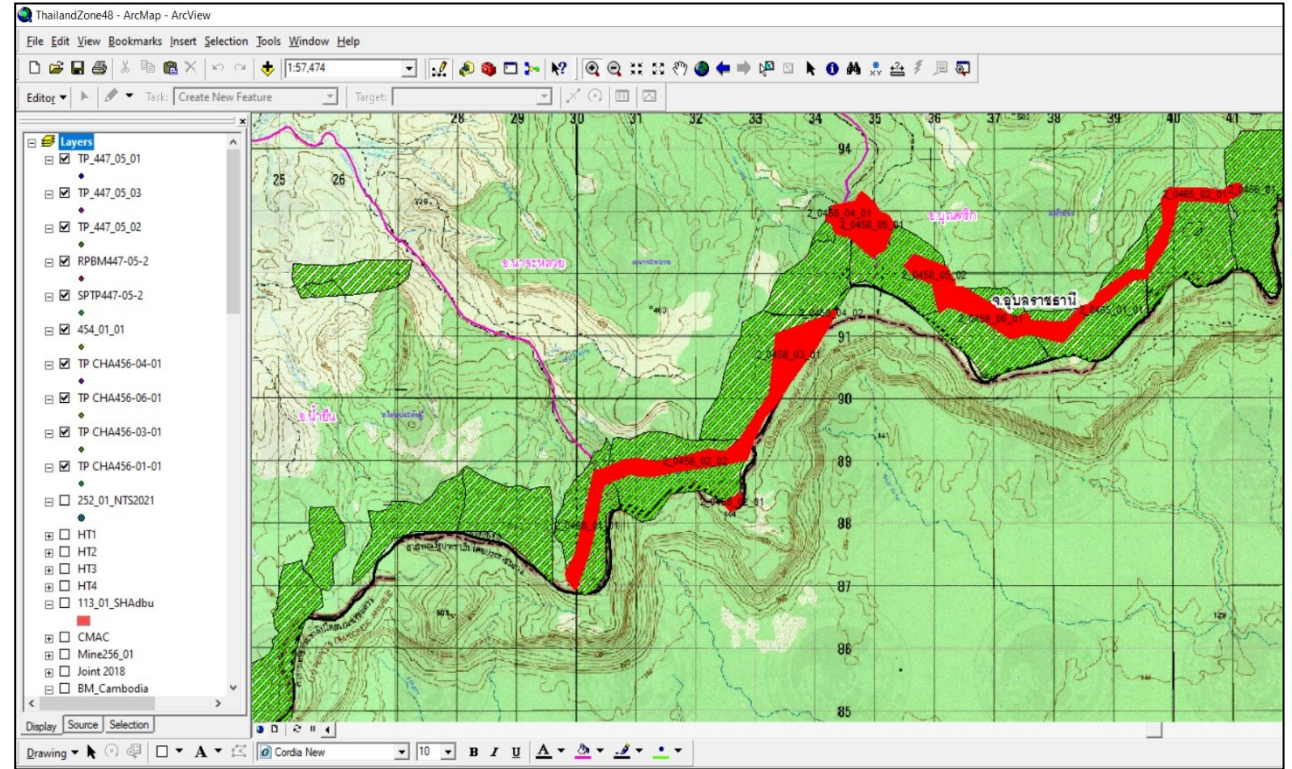

Information Management (ARC GIS containing visual display of data)



Thai Government Funding

Fiscal Year	Personnel (USD)	Operations (USD)	Additional Fund (USD)	Total (USD)
2018	4,762,986.45	2,088,920.98	139,856.12	6,991,763.55
2019	4,932,657.83	2,088,920.98	210,359.72	7,231,938.53
2020	4,932,657.83	2,088,920.98	280,287.79	7,301,866.59
2021	5,235,783.02	2,014,388.60	306,474.84	7,556,646.46
2022	4,862,080.56	1,873,381.40	79,712.23	6,815,174.19
2023 June 2022	4,860,681.53	1,869,965.48	66,168.34	6,796,815.35

Exchange rate 1 USD = 34.76 THB * On 10 June 2022



Enhancing International Cooperation at all levels

2020 Thailand - Cambodia Pilot Project





Challenges towards the Completion of the Mine Clearance Operations

- High level of mine contamination and challenging geographical landscape
- The COVID - 19 Pandemic
- Access to the areas along the border





(High level of Mine Contamination and Challenging

Unusual Landmine Contamination in a Challenging Geographical Landscape



Ruang Phueng
Operation 2020





The COVID -19 Impact





Access to the Areas along the Border





Work Plan for the Requested Extension Period (2023-2026)

Three-Year Work Plan : Thailand's Milestones

Outputs	Phase 1 (Nov 2023 - Oct 2024)	Phase 2 (Nov 2024 - Oct 2025)	Phase 3 (Nov 2025 - Dec 2026)
Size (sqm)	5,328,050	5,149,998	3,563,339

AD3 Year Plan											
No	Description AD	Province	District	Subdistrict	Village	See	Year1	Year2	Year3	Total	Remarks
1	840/AD	SiKao	Taphae	Thpsadt	Rnsai	30462			30462	30462	
2	840/AD	SiKao	Taphae	Thpsadt	Rnsai	90			90	90	
3	110/AD	SiKao	Taphae	Taphae	Thpsiam	10106			10106	10106	
4	110/AD	SiKao	Taphae	Taphae	Thpsiam	10200			10200	10200	
5	550/AD	SiKao	Taphae	Taphae	KhoLucheng	66366			66366	66366	
6	1090/AD	SiKao	Taphae	Taphae	Nonsrikoon	88200		88200		88200	
7	601/AD	SiKao	Kheung	Kheung	Nongkeao	116906		116906		116906	
8	270/AD	SiKao	Kheung	Nomakun	Nonghen	9800		9800		9800	
9	601/AD	SiKao	Aanyasat	Rai	Phumkang	90542		90542		90542	
10	1130/AD	SiKao	Aanyasat	Rai	Rai	148174		148174		148174	
10	10	SiKao				586244	240726	217406	129028	586244	
11	2270/AD	Tiat	Kongai	Halek	Halek	5856			5856	5856	
12	2270/AD	Tiat	Kongai	Halek	Halek	2628			2628	2628	
13	2801/AD	Tiat	Kongai	Halek	Konghin	142580		142580		142580	
14	2290/AD	Tiat	Kongai	Halek	Konghin	36462		36462		36462	
15	2801/AD	Tiat	Kongai	Halek	Kolsi	48366		48366		48366	
16	2801/AD	Tiat	Kongai	Halek	Kolsi	10980		10980		10980	
17	2520/AD	Tiat	Maengat	Chenak	Chenak	46680		46680		46680	
7	7	Tiat				282736	96256	179002	65134	282736	
18	3560/AD	Buri Ram	Barkut	BungChroen	Saichathana	18408		18408		18408	
19	3570/AD	Buri Ram	Lahensi	Nongang	Phaihuayon	61284		61284		61284	
20	3570/AD	Buri Ram	Lahensi	Nongang	Phaihuayon	14004		14004		14004	
21	3570/AD	Buri Ram	Lahensi	Nongang	Phaihuayon	17122		17122		17122	
4	4	Buri Ram				20880		20880		20880	
22	3801/AD	Suin	Kabong	Taken	Sakphathana	2858		2858		2858	
23	4130/AD	Suin	Kabong	Din	Din	2238		2238		2238	
24	4130/AD	Suin	Kabong	Din	Chongkhekor	48242		48242		48242	
25	4130/AD	Suin	Kabong	Din	Chongkhekor	10200		10200		10200	
26	3501/AD	Suin	Phromlongk	Baki	Thaisatuk	60288		60288		60288	
5	5	Suin				246407	162288	28128		246407	
27	4601/AD	S Slet	Kathasak	Sathonghai	Phunsan	108066			108066	108066	
28	4601/AD	S Slet	Kathasak	Sathonghai	Phunsan	3422			3422	3422	
29	4601/AD	S Slet	Kathasak	Sathonghai	Phunsan	78767			78767	78767	
30	4890/AD	S Slet	Kathasak	Laki	No	10380		10380		10380	
4	4	S Slet				229484		10380	218805	229484	
31	4570/AD	UbonRatchaburi	Namkun	Song	Namkun	30104		30104		30104	
1	1	UbonRatchaburi				30104		30104		30104	
31	31	Total				1400137	538000	518988	356339	1400137	



Activities to be carried out

- Pilot project with Cambodia
- Cooperation at other partners at all levels
- Mine Risk Education (MRE) and Victim Assistance (VA)



2 มี.ค.63: การลงนามในเอกสารบันทึกและการสำรวจพื้นที่
“โครงการนำร่องความร่วมมือในการเก็บกู้ทุ่นระเบิดตามแนวชายแดน ไทย-กัมพูชา”





MRE Efforts during the 2nd Extension

Period	No. of MRE Activities	No. of Participants
Phase 1 (2019 - 2020)	315	62,389
Phase 2 (2021	322	21,432





Plan for Mine Risk Education in Border Areas 2024 - 2026

2024			
Unit	Province	District	No. of Times
HMAU 1	Sa Kaeo	Ta Phraya	12
		Khok Sung	12
		Aranyaprathet	12
Total			36
HMAU 2	Trat	Khlong Yai	7
		Mueang Trat	8
	Chanthaburi	Tha-mai	1
		Pongnamron	10
Total			26
HMAU 3	Ubon Ratchathani	Nam Yuen	26
Total			26
HMAU 4	Phetchabun	Khao-kho	8
	Uttaradit	Bankhok	10
	Nan	Chalermphra kiat	2
		Mae Jrim	2
Total			22
HMAU TMAC	Buri Ram	Lahansai	9
		Bankruat	3
Total			12
Grand Total			122

2025			
Unit	Province	District	No. of Times
HMAU 1	Sa Kaeo	Ta Phraya	12
		Khok Sung	12
		Aranyaprathet	12
Total			36
HMAU 2	Trat	Khlong Yai	8
		Mueang Trat	7
	Chanthaburi	Tha-mai	1
		Pongnamron	9
		Soi-dao	1
Total			26
HMAU 3	Si Sa Ket	Kanthralarak	20
Total			20
HMAU 4	Phayao	Phu-sang	2
		Chiangkham	2
		Pong	2
	Tak	Umphang	10
	Chiang Rai	Wiangkan	2
		Mae fah luang	4
Total			22
HMAU TMAC	Buri Ram	Lahansai	9
		Bankruat	3
Total			12
Grand Total			116

2026			
Unit	Province	District	No. of Times
HMAU 1	Sa Kaeo	Ta Phraya	12
		Khok Sung	12
		Aranyaprathet	12
Total			36
HMAU 2	Trat	Khlong Yai	7
		Mueang Trat	7
	Chanthaburi	Tha-mai	1
		Pongnamron	8
		Soi-dao	1
Total			24
HMAU 3	Si Sa Ket	Kanthralarak	10
		Khun-han	10
Total			20
HMAU 4	Mae Hong Son	Mueang	4
		Khun-yuam	2
		Pang-ma-pha	2
		Pai	2
	Chiang Mai	Mae-ai	8
		Chiang-dao	4
Total			22
HMAU TMAC	Buri Ram	Lahansai	9
		Bankruat	3
Total			12
Grand Total			114



Thailand's Commitment Towards Fulfilling Art 5 Obligations

